Kanban and contribution evidence

Adaptive Focus Studio, Mobile App Development Project 1. Howard Fletcher (sole developer, undergraduate pathway).

Repo: https://github.com/Howflet/Adaptive-Focus-Studio
Board: https://app.clickup.com/90141788557/v/b/li/901422483479
File: docs/Kanban_Contribution_Evidence.pdf (also in the final ZIP)


This file is meant to be readable offline, so the board evidence is included as pictures and tables and doesn't need a ClickUp login to check. The board is private to my ClickUp workspace. The snapshots only show my own workspace name and the card titles, no other people or personal data.

1. Board policies I followed


Policy	What I did
Columns	To Do, In Progress, In Review, Complete.
Work in progress limit	At most 2 cards in In Progress and 2 in In Review.
Ownership	Solo project, so every card is mine.
Definition of done	A card goes to Complete only after its pull request is merged and the tests pass.
Branches	One feature branch per card, merged through a pull request (PRs 1 to 11).
Board updates	I moved cards as work progressed, but the dates drifted. See section 5.

2. Dated snapshots


The guide asks for four dated snapshots. I have three real screenshots, taken on the days shown (Oct 20, Oct 23 and Oct 31). I did not take an Oct 24 or Oct 27 snapshot, and I'm not going to backdate anything.

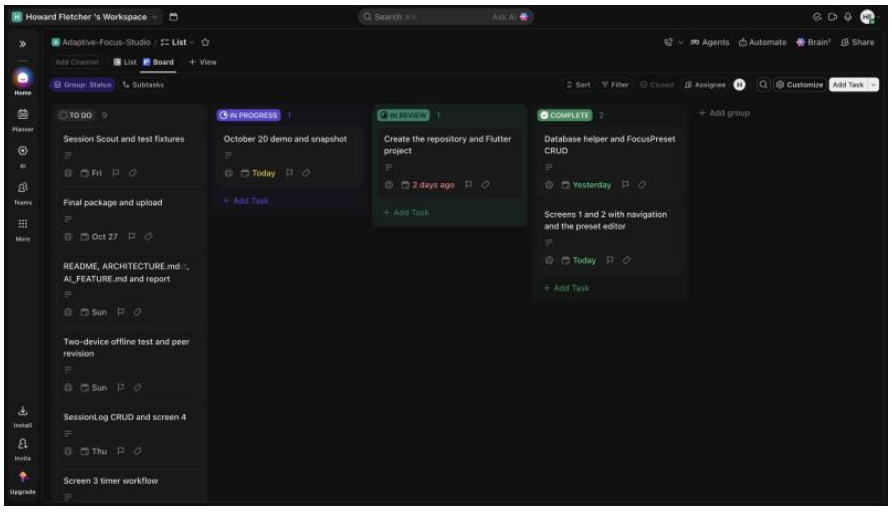

Snapshot 1, Oct 20, 2026. 2 cards complete, 1 in review, 1 in progress, 9 to do.

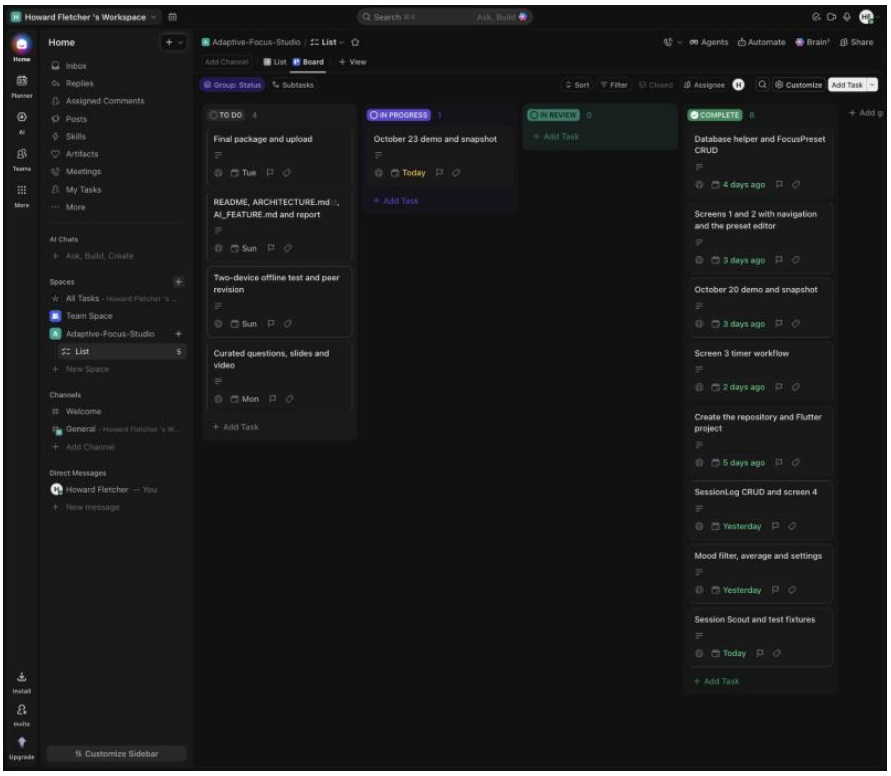

Snapshot 2, Oct 23, 2026. 8 cards complete, 1 in progress, 4 to do.

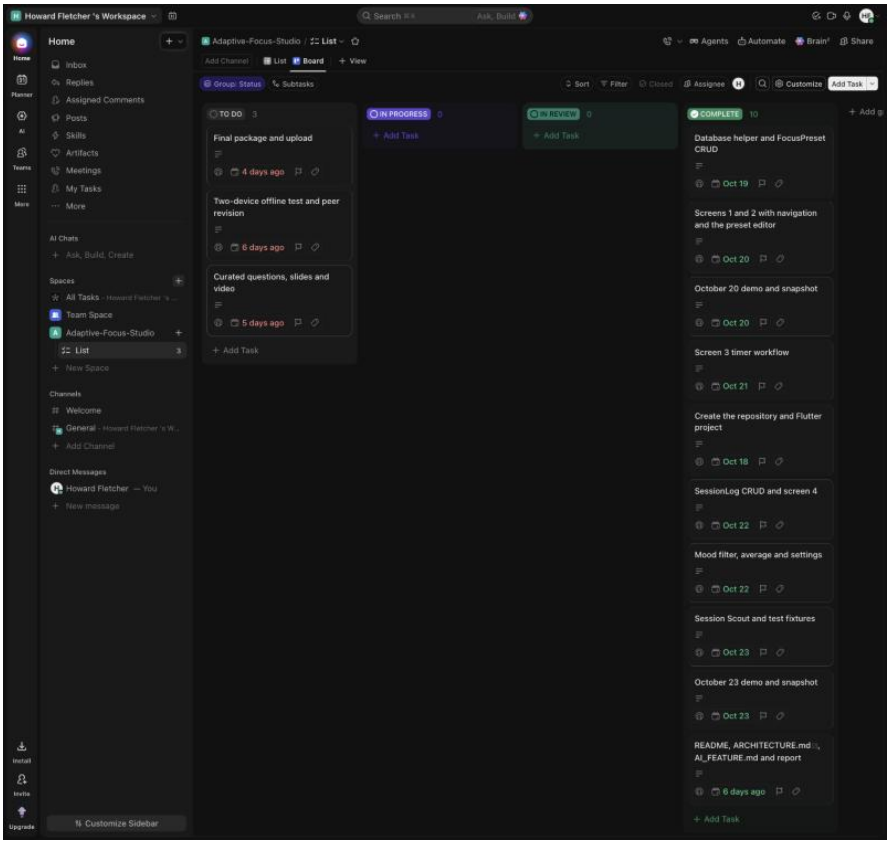

Snapshot 3, Oct 31, 2026. 10 cards complete, 3 to do (all three overdue).

Board status on Oct 31, 2026 (read from the ClickUp list, 13 cards)

Card	Due	Done	Status
Create the repository and Flutter project	Oct 18	Oct 20	complete
Database helper and FocusPreset CRUD	Oct 19	Oct 20	complete
Screens 1 and 2 with navigation and the preset editor	Oct 20	Oct 20	complete
October 20 demo and snapshot	Oct 20	Oct 20	complete
Screen 3 timer workflow	Oct 21	Oct 20	complete
SessionLog CRUD and screen 4	Oct 22	Oct 23	complete
Mood filter, average and settings	Oct 22	Oct 23	complete
Session Scout and test fixtures	Oct 23	Oct 23	complete
October 23 demo and snapshot	Oct 23	Oct 25	complete
README, ARCHITECTURE.md, AI_FEATURE.md and report	Oct 25	Oct 31	complete
Two-device offline test and peer revision	Oct 25	-	to do
Curated questions, slides and video	Oct 26	-	to do
Final package and upload	Oct 27	-	to do

Same data as snapshot 3, read from ClickUp.

3. Task to code to test trace: Session Scout

Card: **Session Scout and test fixtures** (ClickUp 86bcnqgdb), due Oct 23, completed Oct 23. Pull request 7, merged Oct 23.

Step	Evidence
Task	Rule-based helper that suggests a starting duration from my own finished sessions, with a baseline, a reason and user control.
Branch and PR	feature/session-scout, pull request 7 (merge conflict with the settings branch fixed by keeping both imports in the editor, commit 519b49c).
Code	644406d Session Scout function with the 25 min baseline (lib/helpers/session_scout.dart) c2b4e4b Session Scout card widget (lib/widgets/scout_card.dart)
Test	744e868 tests for cases C1 to C6 and a small evaluation (test/session_scout_test.dart, test/fixtures/scout_fixtures.dart) bc72c28 editor tests for the card, Apply and repeated taps (test/scout_card_test.dart)
Result	All of them pass in flutter test (56 tests in the whole project). On the 6 made-up cases Scout's mean absolute error is 7.0 min vs 16.0 min for the 25 min baseline. Details and the 20, 25, 58 counterexample are in AI_FEATURE.md.
Board	Card moved to Complete after PR 7 merged.

4. Commit history

52 commits on main as of Oct 31: 26 on Oct 20, 17 on Oct 23, 1 on Oct 25, 4 on Oct 27 and 4 on Oct 31. Commits are not spread evenly (see below). Full history: https://github.com/Howflet/Adaptive-Focus-Studio/commits/main

PR	Merged	What
1	Oct 20	Database helper and FocusPreset CRUD

PR	Merged	What
2	Oct 20	Screens 1 and 2: presets list and preset editor
3	Oct 20	Oct 20 board snapshot
4	Oct 20	Screen 3: focus session timer
5	Oct 23	SessionLog CRUD and screen 4 (history)
6	Oct 23	Settings screen and SharedPreferences
7	Oct 23	Session Scout helper and test fixtures
8	Oct 25	Oct 23 board snapshot
9	Oct 31	README, ARCHITECTURE.md, AI_FEATURE.md and report
10	Oct 31	Fix settings not saving in the release apk (found on the S22)
11	open	Emulator test results and note that the peer observation was skipped

5. Honest notes, blockers and a flow improvement

What went wrong with the board. The repository card was finished two days after its due date and the database helper card one day after. Then most of the work landed on just two days (Oct 20 and Oct 23), so the board dates don't show steady progress. The Oct 24 and Oct 27 snapshots were missed, and the docs, device testing and final package happened after the Oct 27 deadline.

Blockers. The instructor's GitHub username wasn't known at first, so the invite for the instructor (Silou23) is still waiting for them to accept. A release-only bug (settings not saving, caused by R8 shrinking) was found late by testing on a real phone and fixed in PR 10.

Flow improvement I would make. Cut cards smaller (one screen or one table per card) and move the card the same day its PR merges. That would have kept the dates honest and spread the commits across more days. I have not applied it to this project, since the work is finished, so I'm listing it as the change for next time and not as one I tested.
